




Weekly Project Photos – 02/05/16



Date: 02/01/16  
Building paper and metal lath installed at South bubble wall adjacent to entrance to the Library.



Date: 02/01/16  
JP Witherow loading roofing material onto roof in preparation for start of work.

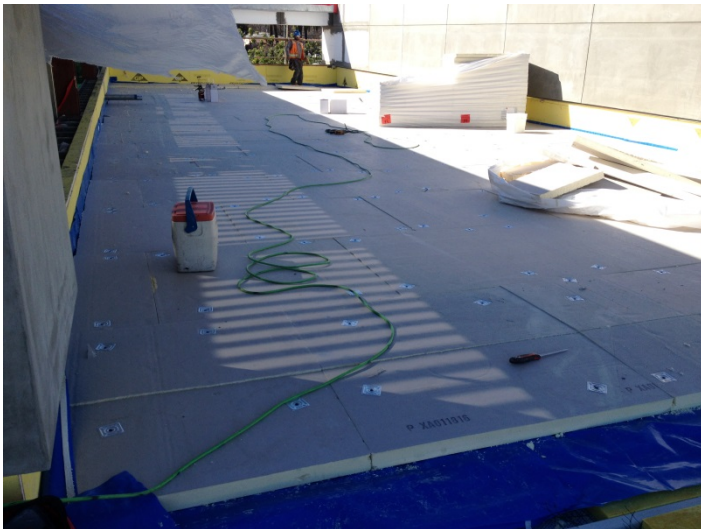

Date: 02/02/16  
Progress of roofing installation by JP Witherow in courtyard area. First layer of insulation mechanically fastened to steel deck.



Date: 02/02/16  
WCF installing insulation in between flutes of deck over the teen area.





Date: 02/02/16  
JP Witherow spreading adhesive prior to installing second layer of insulation for roofing system.



Date: 02/02/16  
Rutherford applied Skim-it coat to EIFS in preparation for final coat application.



Date:02/03/16  
Roofing membrane applied over courtyard area between mechanical well and adult high roof.



Date: 02/03/16  
JP Witherow continuing with roof installation over teen area.



Date:02/04/16

Progress of roofing installation above teen area. Installed Densdeck adhered to second layer of isolation.



Date:02/04/16

Rutherford continuing with foam board installation at the entrance to the Library at the South end of the building.
