



Weekly Project Photos – 02/12/16



Date: 02/08/16  
JP Witherow continuing with roofing installation at main roof on East section of building from teen section to classroom.



Date: 02/08/16  
Installed roofing membrane above teen section of the Library.



Date: 02/08/16  
Rutherford taping reveal joints in preparation for scratch coat application.



Date: 02/09/16  
Progress of roofing installation on East half of library, from teen section extending to classroom.



Date: 02/09/16  
JP Witherow continuing with roofing installation at South end, above children's section / main restroom location.



Date: 02/09/16  
EIFS crew covering South end of library in preparation for rasping of installed foam board.



Date:02/10/16  
Rutherford applying scratch coat of plaster at the exterior of the building.




Date: 02/10/16  
Applied plaster scratch coat at East face of the building, exterior of book drop off location.



Date:02/11/16

Rutherford continuing with installation of gypsum board in the interior of the building.

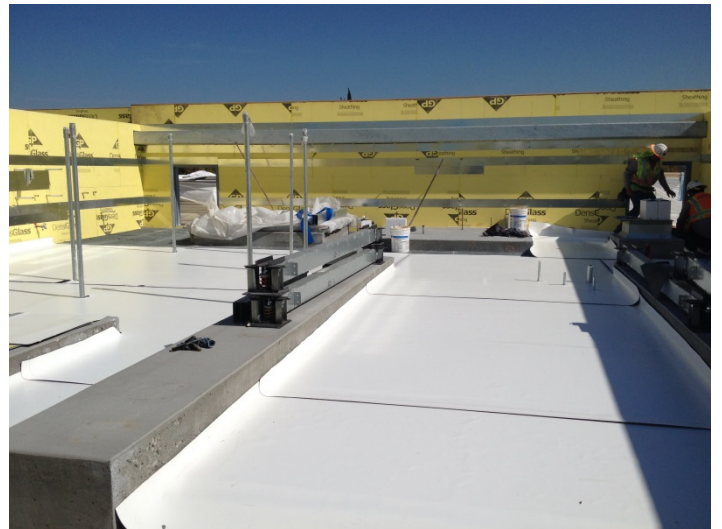

Date:02/11/16

Progress of roofing installation at mechanical well.
